



**British  
Geological Survey**

NATURAL ENVIRONMENT RESEARCH COUNCIL

# BGS cruise to Rockall-Hatton-Faroes region Project 06/02 RRS Charles Darwin CD180 Operations Report

Marine Coastal and Hydrocarbons Programme

Internal Report IR/06/076





BRITISH GEOLOGICAL SURVEY

MARINE COASTAL AND HYDROCARBONS PROGRAMME

INTERNAL REPORT IR/06/076

# BGS cruise to Rockall-Hatton-Faroes region Project 06/02 RRS Charles Darwin CD180 Operations Report

The National Grid and other Ordnance Survey data are used with the permission of the Controller of Her Majesty's Stationery Office.  
Licence No: 100017897/2005.

D. J. Smith

## *Keywords*

Report; Marine; Geophysical, Seismic Reflection; Magnetics, Gravity; Swath; Multibeam; Operations; CD180; BGS06/02; Airgun; Sparker.

## *Contributor/editor*

K. Hitchen, H. Stewart, D.G.Wallis

## *Front cover*

RRS Charles Darwin, Village Bay, St Kilda.

## *Bibliographical reference*

SMITH, D.J., . 2006. BGS cruise to Rockall-Hatton-Faroes region Project 06/02 RRS Charles Darwin CD180 Operations Report. *British Geological Survey Internal Report*, IR/06/076. 48pp.

Copyright in materials derived from the British Geological Survey's work is owned by the Natural Environment Research Council (NERC) and/or the authority that commissioned the work. You may not copy or adapt this publication without first obtaining permission. Contact the BGS Intellectual Property Rights Section, British Geological Survey, Keyworth, e-mail [ipr@bgs.ac.uk](mailto:ipr@bgs.ac.uk). You may quote extracts of a reasonable length without prior permission, provided a full acknowledgement is given of the source of the extract.

Maps and diagrams in this book use topography based on Ordnance Survey mapping.

© NERC 2006. All rights reserved



Loanhead, Edinburgh British Geological Survey 2006

## BRITISH GEOLOGICAL SURVEY

The full range of Survey publications is available from the BGS Sales Desks at Nottingham, Edinburgh and London; see contact details below or shop online at [www.geologyshop.com](http://www.geologyshop.com)

The London Information Office also maintains a reference collection of BGS publications including maps for consultation.

The Survey publishes an annual catalogue of its maps and other publications; this catalogue is available from any of the BGS Sales Desks.

*The British Geological Survey carries out the geological survey of Great Britain and Northern Ireland (the latter as an agency service for the government of Northern Ireland), and of the surrounding continental shelf, as well as its basic research projects. It also undertakes programmes of British technical aid in geology in developing countries as arranged by the Department for International Development and other agencies.*

*The British Geological Survey is a component body of the Natural Environment Research Council.*

### **Marine Operations and Engineering, 2A Nivensknowe Road, Loanhead, Midlothian EH20 9AU**

☎ 0131-448-2700 Fax 0131-448-2545  
e-mail: [djsm@bgs.ac.uk](mailto:djsm@bgs.ac.uk)

### *British Geological Survey offices*

#### **Keyworth, Nottingham NG12 5GG**

☎ 0115-936 3241 Fax 0115-936 3488  
e-mail: [sales@bgs.ac.uk](mailto:sales@bgs.ac.uk)  
[www.bgs.ac.uk](http://www.bgs.ac.uk)  
Shop online at: [www.geologyshop.com](http://www.geologyshop.com)

#### **Murchison House, West Mains Road, Edinburgh EH9 3LA**

☎ 0131-667 1000 Fax 0131-668 2683  
e-mail: [scotsales@bgs.ac.uk](mailto:scotsales@bgs.ac.uk)

#### **London Information Office at the Natural History Museum (Earth Galleries), Exhibition Road, South Kensington, London SW7 2DE**

☎ 020-7589 4090 Fax 020-7584 8270  
☎ 020-7942 5344/45 email: [bgs\\_london@bgs.ac.uk](mailto:bgs_london@bgs.ac.uk)

#### **Forde House, Park Five Business Centre, Harrier Way, Sowton, Exeter, Devon EX2 7HU**

☎ 01392-445271 Fax 01392-445371

#### **Geological Survey of Northern Ireland, Colby House, Stranmillis Court, Belfast BT9 5BF**

☎ 028-9038 8462 Fax 028-9038 8461

#### **Macleans Building, Crowmarsh Gifford, Wallingford, Oxfordshire OX10 8BB**

☎ 01491-838800 Fax 01491-692345

#### **Columbus House, Greenmeadow Springs, Tongwynlais, Cardiff, CF15 7NE**

☎ 029-2052 1962 Fax 029-2052 1963

### *Parent Body*

#### **Natural Environment Research Council, Polaris House, North Star Avenue, Swindon, Wiltshire SN2 1EU**

☎ 01793-411500 Fax 01793-411501  
[www.nerc.ac.uk](http://www.nerc.ac.uk)

## Foreword

This report covers the operation of last scientific cruise for NERC of the RRS Charles Darwin, CD180, BGS Project 06/02, a regional marine geophysical survey west of Scotland, carried out from 20<sup>th</sup> May to 9<sup>th</sup> June 2006. This field operation continues the regional geological mapping in this area that was initiated in 1992 as part of the BGS Rockall Continental Margin Project, but also concentrated on certain specific structures and target areas, which had been identified from previously collected data. The cruise was funded through the BGS Science Budget programme.

## Acknowledgements

As with any offshore work programme, this project was a team effort, with each and every person playing their full part in the continuous 24-hour operations. A full list of the BGS personnel taking part is included in Appendix 1 and their contribution to the success of the operation is hereby acknowledged. Grateful thanks are also due to Captain Peter Sarjeant, the other officers and crew of the RRS Charles Darwin, the technical support provided by Gareth Knight and colleagues of UKORS and Andy Louch and colleagues of the RSU logistical support, for their efforts and assistance to make this an efficient and smooth operation. Thanks also to Ken Hitchen and for the report review.

# Contents

<b>Foreword</b> .....	<b>i</b>
<b>Acknowledgements</b> .....	<b>i</b>
<b>Contents</b> .....	<b>ii</b>
<b>Summary</b> .....	<b>iv</b>
<b>1 Introduction</b> .....	<b>5</b>
<b>2 Narrative</b> .....	<b>5</b>
2.1 Mobilisation.....	5
2.2 Survey .....	5
<b>3 Equipment used</b> .....	<b>8</b>
3.1 Airgun system.....	8
3.2 Sparker system.....	10
3.3 Gravity Meter .....	10
3.4 Magnetometer.....	11
3.5 Multibeam.....	12
3.6 Pinger.....	12
3.7 Precision Echosounder .....	13
<b>Appendix 1 Ship’s complement</b> .....	<b>14</b>
<b>Appendix 2 Summary Daily Log</b> .....	<b>15</b>
<b>Appendix 3 Line Summary Log Sheet</b> .....	<b>39</b>
<b>Appendix 4 Gravity Base Ties</b> .....	<b>40</b>
Corrected Ship Base .....	40
Calculated Drift .....	40
<b>Appendix 5 Time Utilisation Diagrams</b> .....	<b>43</b>
Time Utilisation in the survey area .....	43
Time Utilisation for total ship time .....	43
<b>Abbreviations</b> .....	<b>44</b>

**PLATES**

Plate 1 Deployment of Airguns and 30m hydrophone streamer .....	8
Plate 2 Screen images of Airgun and Sparker data .....	9
Plate 3 Seismic reflection recording layout and hardcopy printer .....	9
Plate 4 Sparkarray and hydrophone 10m hydrophone streamer on an exceptional calm day .....	10
Plate 5 Gravity meter and recording PC .....	11
Plate 6 Deployment of marine magnetometer .....	11
Plate 7 Simrad EM12 multibeam recording and processing .....	12
Plate 8 PES (port) and Pinger (Starboard) .....	12

## Summary

This report describes the operation for BGS Project 06/02 (Charles Darwin CD180), from the mobilisation on the 18<sup>th</sup> May, the regional marine geophysical survey west of Scotland, 24<sup>th</sup> May to 7<sup>th</sup> June and demobilisation on 9<sup>th</sup> June.

The operational aims of the survey project were:

- To carry out a planned programme of 1900 km of marine geophysical surveying to link into existing data

The survey was designed to address several geological objectives including:

- Define size/shape of basalt window;
- Identify and/or constrain compressional folds/faults/thrusts
- Investigate the seismo-stratigraphy of the Faroe-Bank Channel with a view to identifying suitable potential borehole location(s).

The above work was completed ahead of schedule, thus allowing high-resolution seismic reflection lines to be run just south of St Kilda and Stanton Bank.

The geophysical techniques employed were high-resolution single channel seismic reflection, (Airgun and Sparker), gravitational field, magnetic field and multibeam bathymetry. All systems were digitally recorded, and in addition, airgun was digitally processed on line.

The vessel utilised was the RRS Charles Darwin Cruise CD180. The vessel provided an excellent platform for the work involved with good laboratory space, working deck space, general facilities and experienced officers and crew.

The main mobilisation took place between the 18<sup>th</sup> – 19<sup>th</sup> May 2006, in Falmouth, Cornwall. Operations were conducted over a 15-day period and demobilisation took place on the 9<sup>th</sup> June in Fairlie on the Clyde Estuary. Weather conditions varied; there were very few excellent days. There was one day lost to weather and lower quality data was accepted for some of the lines.

The survey was extremely productive with the entire planned programme being completed in 11 days. Additional lines were run just south of St Kilda and Stanton Bank, totalling 30 lines and 2183 km of data.



# 1 Introduction

The British Geological Survey Project 06/02 was a marine geophysical survey (seismic reflection, gravitational field, magnetic field, multibeam bathymetry) covering areas from Rockall, Hatton Bank, the banks south west of the Faroe Islands and the Faroe Bank Channel. The survey was designed to address several geological objectives including:

- Rockall to Hatton Bank: Multibeam only to get full picture from sea-bed to depth (line is coincident with existing BGS seismic collected in 2000 which shows a variety of interesting features).
- Small area on Hatton Bank: Lines across basalt window to define size and shape of window and orientation of fold axes in Mesozoic.
- NW edge of Hatton Bank: Lines across SEA7 sites where video of coral obtained. Lines to investigate if there is relationship between coral growth and geological structure.
- NW edge of Hatton Bank: Lines anticipated to image geological structures some of which might be compressional in origin. Lines cross sea-bed ridges imaged by Spanish 2005 multibeam survey. Origin of ridges unknown (yet).
- Various banks south west of Faroe Islands: Lines designed to investigate the structure of major banks and Wyville-Thomson and Ymir ridges. One line crosses 'Alpin Dome' between Rosemary Bank and Bill Bailey's Bank
- Faroe Bank Channel: Lines mainly to investigate seismic stratigraphy and sediment patterns in Faroe Bank Channel. Also to look for possible future borehole location(s).
- St Kilda: Short high resolution lines were run just south of St Kilda to tie in an existing piston core to existing BGS Deep Tow Boomer line.
- Stanton Bank: High resolution seismic reflection line were run for the MESH project to compliment previously acquired data in 2005 on project BGS 05/05 (CD174).

## 2 Narrative

### 2.1 MOBILISATION

The mobilisation of the RRS Charles Darwin started on 18<sup>th</sup> May in Falmouth and went according to plan apart from damage to the sparkarray power cable that occurred whilst the 10ft bangbox container was unloaded from the lorry.

### 2.2 SURVEY

#### Saturday 20<sup>th</sup> May

The vessel sailed at 10:00 for the final NERC scientific cruise of the RRS Charles Darwin. The prevailing poor weather, and the forecast received, dictated that the best course for the vessel to reach the starting point of the work programme, Rockall, would be through the Irish Sea. Even by taking this course instead of the Atlantic side of Ireland the sea state was poor and uncomfortable for all. Total power loss to the vessel was experienced at 23:00, cause at the time unknown. Power was restored within 15mins.

**Tuesday 23<sup>rd</sup>**

Despite the uncomfortable ride the vessel made good progress arriving SE of Rockall Bank at 07:00. The speed of sound was checked with a sound velocity probe (SVP) to provide a speed of sound through the water column for the multibeam system. This was followed by running lines to check the calibration of the multibeam, heading west up the slope of Rockall Bank. Unfortunately due to the sea state the vessel could not run the reciprocal line down the slope. However a line reciprocal to the down slope line was run back up the slope. Unfortunately the vessel lost total power for the second time in 18 hours, this corrupted the multibeam data and so the check could not be made. By this time the vessel could not make headway due to the increase in swell and wind. The vessel was weathered off. On advice from Gareth Knight, it was decided that further checks would not be attempted to the multibeam, as the calibration was unlikely to be affected from the previous time the multibeam was used.

**Wednesday 24<sup>th</sup>**

By dawn the sea state and wind speed had improved and allowed line 1, a multibeam only line, to start at the designated point approximately 15 miles south of Rockall. Initially the line was run at a speed of 4 knots due to the sea state. The speed was progressively increased throughout the day to the optimum 8 knots.

**Thursday 25<sup>th</sup>**

Line 1 was completed in the morning. The airgun, sparker and magnetometer systems were deployed and up and running in an hour and a half in good sea conditions. Lines 2 to 5 were completed meeting the requirement to image a window within the basalt of Hatton Bank. Problems with compressor 2 overheating did not affect the data collection.

**Friday 26<sup>th</sup>**

Transit to second area of interest on Hatton Bank, lines looking at areas of cold-water coral reefs and geological structures. Lines 6 to 8 are a line running in a generally northerly direction, with small course alterations. On line 10 the vessel had to slow for a time to allow a fishing vessel to pass. By the end of the day part of line 11 had been completed.

**Saturday 27<sup>th</sup>**

Continue on line 11 until completed and all equipment recovered just after 07:00. This completed the area around Hatton Bank. The vessel steamed at 10 knots to the start of a transit line across Lousy, Bill Bailey and Faroe Banks collecting additional multibeam on the way. Note data was collected at 10 knots and not the optimal 8 knots. No line number was given to this opportunist line. The vessel stopped 2 miles before the start of line 12 to perform a SVP deployment followed by deployment of the seismic equipment. Line 12 was started at 20:47.

**Sunday 28<sup>th</sup>**

In the early hours the wind picked up to 25 knots creating a large following swell, which at times broke onto the deck. The sparker was recovered at 05:30 due to poor data and risk to the equipment, the line continued, without break, with airgun. Although the airgun data quality was affected, the vessel was currently on the top of Lousy Bank with little penetration through the basalt. By 10:00 the wind had eased to 13 knots, though still with a large following swell. The swell had diminished enough by 12:30 to re-deploy the sparker, though the data is not of optimum quality. At 14:46 the deepest (1240m) part of the line between the Lousy and Bill Banks was reached. By 16:30 the wind had quickly moved 180 degrees, directly ahead of the vessel and increased to 30 knots. This caused speed fluctuations with the vessel and poor sparker data due to confused sea. The sparker was recovered. Various weather-induced problems followed, magnetometer cable caught on airgun frame, airgun hydrophone noisy, recovered and checked and the vessel found it hard to maintain the required constant speed. The line continued throughout with short loss of airgun data, while the hydrophone was checked and no sparker data for the times it was recovered to deck.

**Monday 29<sup>th</sup>**

Sparker re-deployed in the early hours. At 08:46 the shallowest (88m) part of the Faroe Bank on this line was reached, wind still blowing 16 knots from the north. The line was completed at 20:03 and all equipment was recovered. An SVP was deployed whilst several airguns were changed out, the airgun frame welded up and the sparker trimmed.

**Tuesday 30<sup>th</sup>**

By midnight all equipment had been re-deployed and the vessel was turning onto the next line, running SW across the Faroe Bank Channel. Problems with the airgun hydrophone being entangled with the airgun frame resulted in the vessel circling the line. Line 13 was started at 01:54. Wind reduced to 10-15 knots throughout the day, the swell slowly followed. An emergency drill practice was undertaken mid-morning and included a safety quiz. By midnight line 14 was two-thirds completed.

**Wednesday 30<sup>th</sup>**

The day started with excellent weather, but by midday the wind had picked up to 17 knots from the south. The day ended approximately two-thirds along line 15 with the wind 15 knots from the southwest.

**Thursday 1<sup>st</sup>**

Line 15 continued, just after midnight a loss of air pressure to the airguns was traced to gun 1. This was isolated. Line 16 started late morning, with the wind and swell on the port stern quarter, 20+ knot winds were recorded throughout the day. The data were acceptable though not excellent with the sparker suffering the most.

**Friday 2<sup>nd</sup>**

Line 16 continued, the wind moving slowly around to west-southwest and varying in speed with squalls up to 25 knots. The vessel began to suffer from increased rolling throughout the day and consequently degradation in the data quality similar to the previous day. Line 16 finished at around 19:00, the sparker was recovered for trimming and re-deployed, line 17 started in an easterly direction, the swell directly astern.

**Saturday 3<sup>rd</sup>**

From midnight the wind ameliorated and the swell followed. During the night it was noticed that the on line airgun printer was failing to print all the shots. This problem continued intermittently for the rest of the survey and could not be specifically traced to either the printer or the CODA system that was sending the data. Line 17 finished at 06:03 and line 18 started immediately after a 45 deg course alteration. The CODA recording system lost the easting navigation input for 3 hours during the morning and the GPS signal produced apparent large jumps in position for an hour in the afternoon. The position recorded on each ping recorded on the CODA cannot be relied upon for this line. Line 18 finished at 15:53 and line 19 started half an hour later in a northerly direction.

**Sunday 4<sup>th</sup>**

Line 19 and 20 were completed and line 21 started all in excellent sea conditions.

**Monday 5<sup>th</sup>**

Line 21 was completed at 16:18, this completing the original survey plan. All equipment was recovered and the vessel steamed towards a position just south of St Kilda.

**Tuesday 6<sup>th</sup>**

Additional time allowed a short excursion around the world heritage site of St Kilda. To use the surplus time available two further work areas were proposed.

- An area just south of St Kilda to run seismic reflection lines across an existing piston core location to tie this into previously run BGS Deep Tow Boomer lines.
- Stanton Bank: To fill in data collected in 2005.

Both these areas required high resolution seismic. Unfortunately no surface tow boomer was on board. The sparker system was adapted to optimise it for high resolution. All tips were made into a line for uniform depth, the power per tip was reduced, flotation was added to try to maintain a tow depth of 0.25 m, the vessel speed was reduced to increase the number of shots per km, the firing interval was reduced from 6 sec to 0.6 sec and the sampling rate and filter frequencies increased.

Work started at the St Kilda area 18:00 and 5 lines (22-26) were completed by 22:00. The equipment run was sparker, PES, pinger and multibeam. The pinger gave good results until the sparker was switched on and obliterated the pinger record. Upon completion all equipment was recovered and the vessel steamed to the next work area at Stanton Bank.

### Wednesday 7<sup>th</sup>

07:30 arrived at Stanton Bank work area. After a short delay waiting for a fishing boat to move away, the first line, 27, was started at 07:54. Four lines (27-30) were completed by 22:00. All equipment was recovered and the vessel steamed towards Fairlie. This concluded the survey.

### Thursday 8<sup>th</sup>

Steaming to Fairlie

### Friday 9<sup>th</sup>

Arrived Fairlie 11:30. Allowed gravity meter to settle before switching off. 14:00 Demob equipment and depart the vessel and travel to Edinburgh.

## 3 Equipment used

### 3.1 AIRGUN SYSTEM


**Source:** An array of 5 x 40 cu inch Bolt 600B airguns with waveshape kits and time break solenoids was utilised as the airgun source. Routinely, up to four guns were fired simultaneously, keeping the fifth gun as a ready spare. The number of guns used varied with water depth, with a minimum of 1 being used in the shallower areas. The firing rate varied from 6 – 7 seconds depending on water depth. The airgun array firing synchronisation was achieved by monitoring the time break solenoids and manually adjusting each airgun's trigger as required. This introduces a short time delay into the system of between 25 and 38 milliseconds and thus the sea-bed return time is not an absolute measurement of depth. A 20ft compressor container belonging to BGS containing two CompAir Reavell type VHP36 compressors supplied the high-pressure air for the airguns. Air was fed from the compressors through the vessel's internal pipe-work to the aft deck and connected into the BGS airgun control panel.



Plate 1 Deployment of Airguns and 30m-hydrophone streamer

**Hydrophone:** A 4 channel SIG hydrophone summed to give a single channel 32m active length was utilised as the receiver for the airgun source.

**Recording:** The BGS CODA DA200, software version 3.9.11.5L(3360) 2005 four-channel digital recording and processing system was utilised to record the raw data. The data were recorded to Flipdisks in CODA format with a sampling frequency of 3kHz, record length of 4 seconds and bandpass filter of 25-800 Hz. The start of recording was delayed in deep water to permit a minimum of 2 seconds of data below the sea-bed. The CODA system also received a navigation data string from the vessels Trimble DGPS system, and logged position, time and date for each shot.

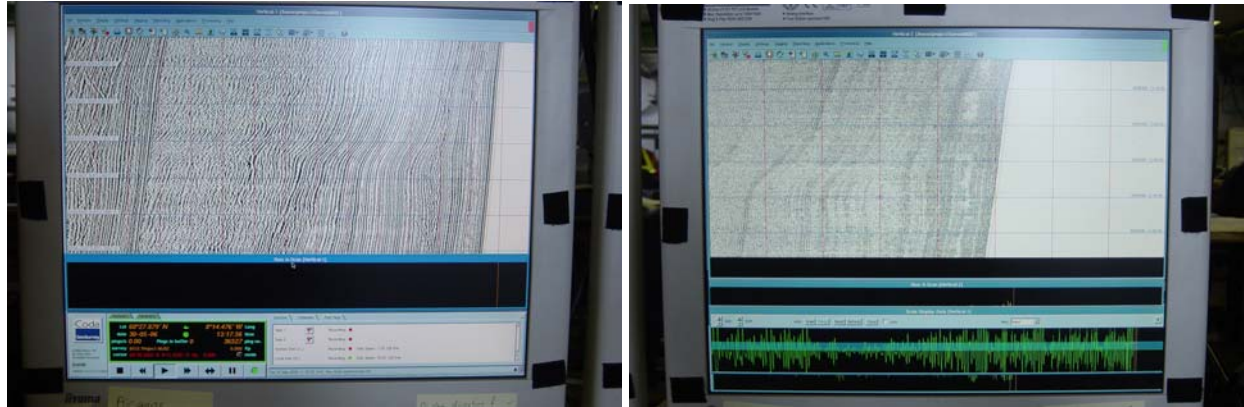

**Plate 2 Screen images of Airgun and Sparker data**

**On line processing:** In addition to the recording described above, the CODA system was also used to process the data on-line and produce a real time hard copy output on an Ultra 120 thermal printer. Processes applied were time varied gain (TVG), time varied filtering (TVF) and trace mixing and, in extremely large amplitude sea swell situations, a swell filter. Both TVG and TVF were applied from the sea-bed, which was tracked automatically. A 1.5 sec record length was used for the on-line hard copy, with a delay adjusted to give an optimum record for the water depth.



**Plate 3 Seismic reflection recording layout and hardcopy printer**



### 3.2 SPARKER SYSTEM

**Source:** EG&G, nine candle, multi-tip sparkarray with 135 tips was utilised as the sparker source.

**High Voltage Power Supply:** An Applied Acoustic Engineering CSP2200 capacitor charging unit. This is a single unit, powered from the ship's 240VAC supply incorporating switchable output energy up to a maximum of 2200 J. Apart from lines 2-5 (1800J) the whole survey was conducted at an output of 2200 J.



**Plate 4 Sparkarray and hydrophone 10m hydrophone streamer on an exceptional calm day**

**Hydrophone:** A seven channel Teledyne 10m hydrophone, summing on the most part, all channels to give a single output, was utilised as the receiver for the sparker source.

**Recording:** This utilised the same CODA DA200 four-channel digital recording and processing system as the airgun, with the data recorded on the same file to Flipdisk in CODA format. The data were recorded with a sampling frequency of 5kHz, record length of 1.9 seconds and a bandpass filter of 100-1730 Hz. The start of recording was delayed in deep water to permit a minimum of 1 second of data below the seabed. As with the airgun, position, time and date were recorded with every shot.

**On-line processing:** The sparker data was processed on line for QA purposes of the recorded data. Processes applied were time varied gain (TVG), time varied filtering (TVF), swell filter (occasionally), and trace mixing. Both TVG and TVF were applied from the sea-bed, which was tracked automatically. A hardcopy output could not be obtained on line as the BGS only has one thermal printer that will operate with the CODA. During long transits and weather downtime hard copies were generated. A 700msec record length was used for the hard copy, with a delay adjusted to give an optimum record in the prevailing water depth. Ideally a second printer would be beneficial on these projects to obtain the on line hardcopies required and as a backup for the only printer.

### 3.3 GRAVITY METER

The gravity meter used was a ZLS Corporation UltraSys controlled LaCoste and Romberg sensor serial No. S75 system. This consists of a highly damped, zero-length spring type gravity sensor mounted on a gyro-stabilised platform, together with associated control and recording electronics. The sensor and control electronics were located in the 'Controlled Temperature Laboratory' adjacent to the 'Main Laboratory', this allowed easy access for observation. It was impractical to mobilise the meter in the vessel's 'Gravity Room' due to access restrictions for

both equipment and cables to main lab. Gravity was measured continuously and the gravity, spring tension and cross coupling correction values were logged at a one second interval in L&R Long Format onto the ship's logging and processing system and internally in the gravity control computer. Additional backup data storage was achieved through utilising the zip drive incorporated with the gravity control computer. Data were also output to a colour printer for QC purposes. No data processing was carried out on the vessel.

The vessel suffered two complete blackouts during the transit to the work area. This resulted in the meter losing power and having to be clamped and kept on heat using a battery powered, power supply. At the time of writing it is unknown if these two power blackouts have had an affect on the data, although this felt unlikely. However it was observed that the internal pressure within the meter varied with atmospheric pressure and this should be corrected for using the approximation of 1mGal for every 4Hpa of pressure change. This fault should be repaired before the next cruise.



**Plate 5 Gravity meter and recording PC**

### 3.4 MAGNETOMETER

The system used was a Barringer proton precession magnetometer with a 1 gamma sensitivity. The sensor was towed 200 m astern to minimise the effects of the vessel's steel hull on the local magnetic field. The system was triggered by the seismic control system such that the sensor was polarising when the sparker fired. This eliminated electrical interference from the sparker discharge. The data were converted from parallel Binary Coded Decimal (BCD) data to serial data within a BCD to serial converter before being logged onto the ship's logging and processing system.

This very elderly system performed as well as can be expected, though suffered from noise on some lines. Consideration should be given to the replacing this ageing system, to a system that is higher resolution and easier to interface and record the data, both hard copy and digital as paper and pens are becoming expensive and difficult to source.



**Plate 6 Deployment of marine magnetometer**

### 3.5 MULTIBEAM

The vessel has an elderly deep water Simrad EM12 multibeam system, which was used throughout the survey. Checks of the multibeam calibration were made when the vessel arrived at Rockall Bank. Lines were run up the bank and down on a reciprocal course. Unfortunately the weather was too severe for the vessel to run an accurate reciprocal course. A further line was run back up the slope, however the data was lost when the vessel had a complete blackout. After half a day of attempting to check the calibration of the multibeam system without success, coupled with the poor weather conditions, it was decided, with advice from the multibeam operator on board that no further attempts would be made. The vessel was weathered off for next 12 hours.

Note: The calibration of the multibeam historically has proven to be stable and as such no recalibration was deemed necessary or was planned for this project. The attempted checks of the multibeam calibration were just that, checks.


Several sound velocity profiles were made throughout the survey, Rockall Bank, before the start of line 12 and the Faroe Bank Channel. It was noted that the Faroe Bank Channel had fresh water close to the seabed.



**Plate 7 Simrad EM12 multibeam recording and processing**

### 3.6 PINGER

The 3.5kHz pinger is a transducer mounted in a tow fish and was towed over the starboard side. This was controlled by an IOS transceiver with the data recorded on a CodaOctopus360 acquisition system and was part of the standard shipboard equipment. The pinger gave poor sub-bottom records compared with the sparker system and was affected by the sparker especially in the St Kilda and Stanton Bank areas where the sparker was fired at the higher rate of 0.6 sec.

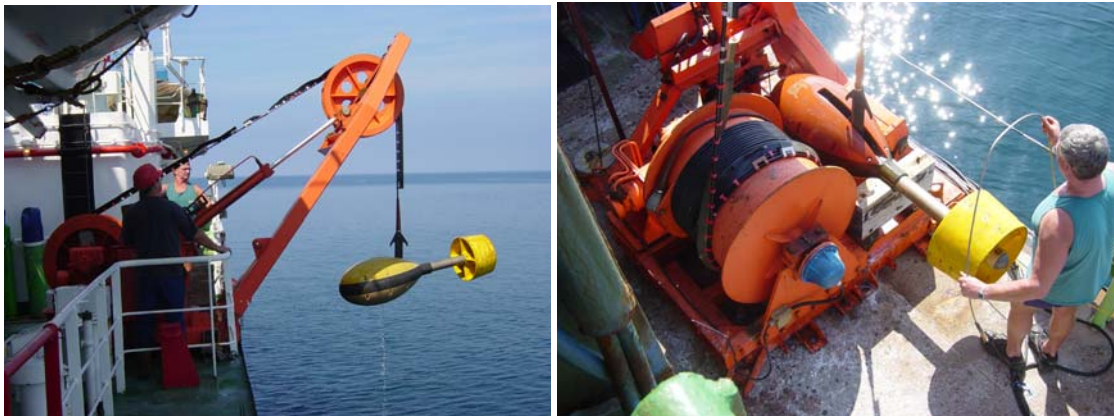

**Plate 8 Recovery of PES (port) and Pinger (Starboard)**



### **3.7 PRECISION ECHOSOUNDER**

The Precision Echosounder (PES) is a 10kHz IOS transducer mounted in a tow fish and deployed off the port side close to amidships. This is controlled by a Simrad EA500 transceiver and display and was compensated for fish height with the depth recorded centrally. Paper printout was only collected for the lines around St Kilda and Stanton Bank.

## Appendix 1 Ship's complement

<b>BGS</b>		<b>RRS Charles Darwin</b>	
Dave Smith	<i>Electronic Engineer-Principal Scientist</i>	Peter Sarjeant	<i>Master</i>
Davie Baxter	<i>Mechanical Engineer</i>	Peter Newton	<i>Chief Officer</i>
Iain Pheasant	<i>Mechanical Engineer</i>	Kieron Hailes	<i>2nd Officer</i>
Heather Stewart	<i>Marine Geologist</i>	Katie Rumbold	<i>3rd Officer</i>
Adrian Tuitt	<i>Student Geologist</i>	John Holt	<i>Chief Engineer</i>
Dave Wallis	<i>Electronic Engineer</i>	Glynn Collard	<i>2nd Engineer</i>
Michael Wilson	<i>Electronic Engineer</i>	John Harnett	<i>3rd Engineer</i>
		David Ardern	<i>3rd Engineer</i>
		John Smyth	<i>Engine Room Petty Officer</i>
		David Holdsworth	<i>Electrical Officer</i>
<b>UKORS, NOC</b>		Michael Minnock	<i>Chief Petty Officer scientific</i>
Gareth Knight	<i>IT Support</i>	Michael Drayton	<i>Chief Petty Officer Deck</i>
		Philip Allison	<i>Petty Officer Deck</i>
		Gerald Cooper	<i>Seaman</i>
		Stewart Barrett	<i>Seaman</i>
		Joseph Lambert	<i>Seaman</i>
		Ford Prefect	<i>Seaman</i>
<b>University of Malaga</b> <b>Instituto Espanol Oceanographie</b>		Paul Lucas	<i>Ship Catering Manager</i>
Miriam Sayago-Gil	<i>Marine Geologist</i>	Darren Caines	<i>Chef</i>
		Wilmot Isby	<i>Assistant Chef</i>
		Jacqueline Paterson	<i>Steward</i>
<b>Guardline</b>			
Len Phillips	Supernumery		

## Appendix 2 Summary Daily Log

All times quoted are GMT

## Summary Daily Log

Date: Thursday 18<sup>th</sup> May 2006

### Time

08:30 Arrive vessel, County Warf, Falmouth, start mobilisation  
 Sparker power cable damaged when 10ft container lifted off lorry  
 16:45 Depart vessel

Total km of completed lines: 0

	Today (hours)	Total (hours)
Mob/demob, setting up	8.25	8.25
On line	0.00	0.00
Turning	0.00	0.00
Steaming	0.00	0.00
Weather downtime	0.00	0.00
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	7.25	7.25

## Summary Daily Log

Date: Friday 19<sup>th</sup> May 2006

Time

08:00 Join vessel, continue mobilisation

12:45 Gravity base-tie at half tide 11811.2 PC

Total km of completed lines: 0

	Today (hours)	Total (hours)
Mob/demob, setting up	10.00	18.25
On line	0.00	0.00
Turning	0.00	0.00
Steaming	0.00	0.00
Weather downtime	0.00	0.00
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	14.00	21.25

## Summary Daily Log

Date: Saturday 20<sup>th</sup> May 2006

Time

09:00 RRS Charles Darwin departs Falmouth for her last scientific cruise for NERC  
Weather poor, head up the Irish Sea

15:15 Emergency drill

Total km of completed lines: 0

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	18.25
On line	0.00	0.00
Turning	0.00	0.00
Steaming	14.00	14.00
Weather downtime	0.00	0.00
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	10.00	31.25

## Summary Daily Log

Date: Sunday 21<sup>st</sup> May 2006

Time

09:30 Scientific briefing

13:00 SIG hydrophone oil topped up  
Sparker finally repaired

Total km of completed lines: 0

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	18.25
On line	0.00	0.00
Turning	0.00	0.00
Steaming	24.00	38.00
Weather downtime	0.00	0.00
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Monday 22<sup>nd</sup> May 2006

### Time

00:00 Vessel passing Dumfries & Galloway, heading for Rockall  
 13:00 Multibeam switched on  
 23:00 Total ship power failure, gravity meter clamped and on backup heater supply  
 23:30 Restart Gravity meter  
 23:50 Gravity meter running

Weather poor throughout the day, vessel rolling and pitching

Total km of completed lines: 0

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	18.25
On line	0.00	0.00
Turning	0.00	0.00
Steaming	24.00	62.00
Weather downtime	0.00	0.00
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25



## Summary Daily Log

Date: Tuesday 23<sup>rd</sup> May 2006

### Time

00:00 On passage to survey area  
 07:15 Hove to and deploy SV probe to obtain sound velocity profile for multibeam  
 Water depth 2066, winching very slow, due to lightweight.  
 10:43 SV probe on deck  
 11:50 Run multibeam up slope towards Rockall Bank, dir NW, to check alignment  
 Deploy pinger, weather deteriorating  
 14:40 Turn vessel and reciprocal line, vessel cannot maintain course due to weather  
 15:45 Run line back up slope on reciprocal course to previous line, dir NW  
 Wind now gusting 35 knots from NW  
 16:26 Total ship power failure, vessel pushed beam on, gravity meter clamped  
 16:32 Vessel power restored, multibeam calibration data lost  
 Vessel cannot make headway in present sea conditions, decide not to rerun checks  
 16:50 Gravity meter operating  
 23:59 Vessel heading towards start of first line, but is effectively hove to due to weather  
 conditions

Total km of completed lines: 0

	Today (hours)	Total (hours)
Mob/demob, setting up	8.75	27.00
On line	0.00	0.00
Turning	0.00	0.00
Steaming	7.25	69.25
Weather downtime	8.00	8.00
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Wednesday 24<sup>th</sup> May 2006

### Time

00:00 Vessel proceeding slowly (2 knots) towards start of K1, sea state poor, 35 knot wind  
 06:32 SOL1, Dir NW, multibeam, PES only  
 23:59 On line 1

Total km of completed lines: 0

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	27.00
On line	17.50	17.50
Turning	0.00	0.00
Steaming	0.00	69.25
Weather downtime	6.50	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Thursday 25<sup>th</sup> May

### Time

00:00 On line 1  
 02:08 Course alteration for final section of line, Dir W-NW deg  
 03:00 Wind 10 knots, westerly, old swell prevailing  
 06:53 EOL 1  
 07:30 Start to deploy airguns  
 09:00 Airguns, sparker and magnetometer systems deployed  
 10:09 SOL 2, Dir SE  
 12:33 EOL 2  
 13:02 SOL 3, Dir NW  
 15:10 EOL 3, Air compressor 2 overheating  
 17:08 SOL 4, Dir SW  
 17:24 Airgun hydrophone deployed further to maintain depth  
 19:00 EOL 4  
 19:17 Compressor 2 shut down, air leak into cooling system  
 20:26 SOL 5, Dir NE  
 21:00 Increase in magnetometer noise  
 22:28 EOL 5, recover sparker for trimming

Total km of completed lines: 367

	Today (hours)	Total (hours)
Mob/demob, setting up	1.50	28.50
On line	15.50	33.00
Turning	5.00	5.00
Steaming	2.00	71.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Friday 26<sup>th</sup> May

### Time

00:00 On transit to next line  
 01:00 Re-deploy sparker  
 01:05 Sparker set to 2200J  
 01:44 SOL 6, Dir N  
 06:10 EOL 6  
 06:12 SOL 7, Dir N, course change from line 6  
 08:35 EOL 7  
 08:38 SOL 8, Dir N, course change from line 7  
 11:14 EOL 8  
 12:00 SOL 9, Dir SE  
 15:28 EOL 9  
 15:53 SOL 10, Dir NE  
 18:27 Slowing to 3 knots for fishing boat  
 18:38 Magnetometer switched off, hauled closer to vessel in response to proximity of fishing vessel  
 18:58 Magnetometer deployed to full length and switched ON  
 20:26 EOL 10  
 21:18 SOL 11, Dir E  
 23:59 On line 11

Total km of completed lines: 499

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	28.50
On line	21.25	54.25
Turning	1.00	6.00
Steaming	1.75	73.00
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Saturday 27<sup>th</sup> May

### Time

00:00 On line 11  
 06:32 EOL 11,  
 07:14 All seismic equipment and magnetometer recovered to deck  
 Steam to next survey area, north-east of Hatton Bank  
 Repair sparker, one candle not firing, replace candle holder  
 Drain air compressor storage tank and clean air filter/scrubber  
 15:30 Arrive 2 miles before next line, recover pinger  
 15:38 Deploy SVP for multibeam calibration  
 16:53 SVP on deck  
 17:00 Pinger deployed  
 17:05 Power to compressors switched ON, waiting for pressure to build up  
 (cannot operate at the same time as winch)  
 18:20 Airguns, sparker and magnetometer deployed  
 18:47 SOL 12, Dir NE  
 23:59 On line 12

Total km of completed lines: 569

	Today (hours)	Total (hours)
Mob/demob, setting up	3.75	32.25
On line	11.75	66.00
Turning	0.25	6.25
Steaming	8.25	81.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Sunday 28<sup>th</sup> May

### Time

00:00 On line 12  
 04:00 Wind 20 knots, sea state 4-5, swell behind vessel  
 05:00 Wind 25 knots, sea state 5, swell building following sea  
 05:30 Swell very large breaking on after deck  
 05:37 Switch off sparker  
 05:47 Sparker and hydrophone recovered, airgun data suffering, but currently on top of Lousy Bank  
 09:23 Wind 13 knots, still large following sea, occasionally breaking over stern  
 12:40 Deployed sparker, slight reduction in sea state, now in trough between Lousy and Bill Bailey Bank  
 16:30 Wind moved around 180 degrees to be ahead of vessel and increased to 30 knots quickly, resulting in opposing swells and confused sea ship movement increased, sparker data poor  
 17:24 Sparker recovered, seastate poor  
 22:03 Vessel struggling to keep on course, current and sea condition resulting in crabbing and magnetometer, cable tangled in airgun frame,  
 22:08 Recover magnetometer and airgun hydrophone to inspect.  
 22:16 Re-deploy airgun hydrophone  
 23:59 On line 12

Total km of completed lines: 569

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	32.25
On line	24.00	90.00
Turning	0.00	6.25
Steaming	0.00	81.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Monday 29<sup>th</sup> May

### Time

00:00 On line 12  
 01:59 Sparker deployed  
 02:06 Magnetometer deployed  
 08:46 Shallowest part of Faros Bank, 88m  
 Wind N, 16 knots, cold, vessel 60m off-track to starboard  
 10:50 Vessel off-track 86m to starboard  
 20:03 EOL 12  
 20:35 All equipment recovered  
 Deploy SVP  
 SVP on deck  
 Transit to next line  
 Slow to deploy geophysics equipment

Total km of completed lines: 944

	Today (hours)	Total (hours)
Mob/demob, setting up	3.00	35.25
On line	20.00	110.00
Turning	0.00	6.25
Steaming	1.00	82.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Tuesday 30<sup>th</sup> May

### Time

00:00 Airgun, sparker and magnetometer deployed  
 00:23 Airgun hydrophone noisy, hydrophone rope tangled in airgun frame  
 Vessel loops around to restart line  
 01:54 SOL 13, dir SW  
 09:30 Emergency drill practice  
 10:30 Turn for dog leg part of line  
 16:23 EOL 13  
 17:03 SOL 14, Dir NE, seastate good  
 23:59 On line 14

Total km of completed lines: 1010

	Today (hours)	Total (hours)
Mob/demob, setting up	2.00	37.25
On line	21.25	131.25
Turning	0.75	7.00
Steaming	0.00	82.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25



## Summary Daily Log

Date: Wednesday 31<sup>st</sup> May

### Time

00:00 On line 14  
 03:45 EOL 14  
 03:26 Sparker recovered for trimming  
 03:44 Sparker deployed  
 04:46 SOL 15, Dir SW, sea-state good  
 13:15 Wind increasing, 17 knots, Dir 190, port quarter  
 15:47 Wind increasing, 23 knots, Dir 190, port quarter, swell increasing  
 16:40 Vessel finding it difficult to maintain set speed, hydrophones changing depths  
 17:48 Wind speed falling, 18 knots, swell  
 20:09 Wind speed falling, 15 knots, swell  
 23:59 On line 15

Total km of completed lines: 1070

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	37.25
On line	23.00	154.25
Turning	1.00	8.00
Steaming	0.00	82.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Thursday 1<sup>st</sup> June

### Time

00:00 On line 15  
 00:21 Loss of pressure on airguns, shut off pressure to airgun 1  
 04:00 Wind increasing, 16 knots, Dir SW, dead ahead  
 06:13 Wind increasing, 20 knots, Dir SW, dead ahead, vessel pitching and finds it  
 Difficult to maintain set speed  
 09:00 21 knot wind, Dir SW, dead ahead, data quality poor  
 10:17 EOL 15, recover sparker for trimming  
 11:02 Wind speed 19 knots, Dir W-SW deg  
 11:22 SOL 16, Dir N  
 11:35 Swell on port stern quarter, move sparker hydrophone to end of boom  
 15:36 Wind Speed 16.5 knots, Dir W-SW  
 21:40 Wind Speed 19.5 knots  
 23:59 On line 16

Total km of completed lines: 1300

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	37.25
On line	23.00	177.25
Turning	1.00	9.00
Steaming	0.00	82.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Friday 2<sup>nd</sup> June

### Time

00:00 On line 16  
 00:48 Wind speed 20 knots, Dir 250 deg  
 02:10 Wind speed 18 knots, Dir 270 deg  
 03:49 Sparker recovered on top of Bill Bailey's Bank and trimmed  
 04:14 Problems with oil filter of air compressor 2, shut down and reduce number of guns firing  
 05:10 Compressor back up and running  
 07:14 Wind speed 20 knots, Dir 265 deg  
 11:33 Wind speed 18 knots, Dir 282 deg  
 14:06 Wind speed 21 knots, Dir 280 deg  
 18:50 Wind speed 18 knots, Dir 290 deg  
 18:58 EOL 16, recover sparker for trimming  
 19:24 Sparker deployed  
 19:44 SOL 17, Dir E  
 20:20 Bridge position making large jumps  
 20:31 Ship back on line  
 22:56 Wind speed 13 knots, Dir 280 deg  
 23:59 On line 17

Total km of completed lines: 1545

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	37.25
On line	22.25	199.50
Turning	1.75	10.75
Steaming	0.00	82.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Saturday 3<sup>rd</sup> June

### Time

00:00 On line 17  
 02:22 On line printer not printing data correctly, missing pings  
 03:45 Wind speed 13 knots, Dir 307 deg  
 04:00 Wind speed 11 knots, Dir 307 deg  
 05:58 Sparker OFF and recovered for trimming  
 06:01 Start to alter course to next line  
 06:03 EOL 17  
 06:16 SOL 18, Dir SE, course alteration complete  
 06:25 Sparker deployed and ON, Printer not printing correctly  
 08:40 08:40 to 11:38, lost easting on CODA NAV.  
 14:50 GPS signal poor, large variations in apparent position  
 15:20 GPS position stable  
 15:53 EOL 18, Sparker recovered for trimming  
 16:13 Sparker deployed  
 16:21 SOL 19, Dir N  
 23:59 On line 19

Total km of completed lines: 1712

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	37.25
On line	23.50	223.00
Turning	0.50	11.25
Steaming	0.00	82.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Sunday 4<sup>th</sup> June

### Time

00:00 On line 19  
 01:46 EOL 19, recover sparker for trimming  
 02:10 Deploy Sparker  
 02:28 SOL 20, Dir SW  
 20:05 Sparker recovered for trimming  
 20:21 EOL 20, deploy sparker  
 20:22 SOL 21, Dir SW  
 22:20 On line printer missing pings  
 23:59 On line 21

Total km of completed lines: 1913

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	37.25
On line	0.00	223.00
Turning	23.25	34.50
Steaming	0.75	83.00
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Monday 5<sup>th</sup> June

### Time

00:00 On line 21  
 10:26 Wind 11 knots, Dir 176 deg  
 16:00 Wind 11.6 knots, Dir 185 deg  
 16:18 EOL 21  
 16:45 All gear recovered, steam toward St Kilda work area  
 Start to replay data

Total km of completed lines: 2073

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	37.25
On line	16.25	239.25
Turning	0.00	34.50
Steaming	7.75	90.75
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	31.25

## Summary Daily Log

Date: Tuesday 6<sup>th</sup> June

### Time

00:00	On transit
10:30	Arrive Village Bay, St Kilda
16:00	Leave St Kilda
18:00	Arrive at St Kilda work area and deploy sparker and hydrophone
18:40	SOL 22, Dir NE
19:06	Cross piston core location, vessel off-track 10m SE of proposed line
19:24	EOL 22
19:50	SOL 23, Dir S
19:58	Cross piston core location, vessel off-track 6.3m W of proposed line
20:11	EOL 23
20:18	SOL 24, Dir N
20:41	EOL 24
20:50	SOL 25, Dir S
21:14	EOL 25
21:44	SOL 26 Dir E
21:56	Cross piston core location, vessel off-track 0.73m N of proposed line
22:04	EOL 26, recover sparker and hydrophone and transit to Stanton Bank
23:59	On transit

Total km of completed lines: 2089

	Today (hours)	Total (hours)
Mob/demob, setting up	0.50	37.75
On line	6.25	245.50
Turning	1.25	35.75
Steaming	14.00	104.75
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	2.00	33.25

## Summary Daily Log

Date: Wednesday 7<sup>th</sup> June

### Time

00:00 Steaming to Stanton Bank  
 07:30 On site waiting for fishing vessel  
 Deploy Sparker and hydrophone  
 07:54 SOL 27, Dir SW  
 10:18 EOL 27  
 10:50 SOL 28, Dir NE  
 12:57 EOL28  
 13:22 SOL 29, Dir SE  
 15:10 EOL 29  
 15:39 SOL 30  
 22:04 EOL 30, end of survey, recover all equipment  
 22:20 All equipment recovered, transit to Fairlie

Total km of completed lines: 2183

	Today (hours)	Total (hours)
Mob/demob, setting up	0.50	38.25
On line	13.00	258.50
Turning	1.50	37.25
Steaming	9.00	113.75
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	33.25



## Summary Daily Log

Date: Thursday 8<sup>th</sup> June

Time

00:00 Transit to Fairlie

23:59 Transit to Fairlie

Total km of completed lines: 2183

	Today (hours)	Total (hours)
Mob/demob, setting up	0.00	38.25
On line	0.00	258.50
Turning	0.00	37.25
Steaming	24.00	137.75
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	33.25

## Summary Daily Log

Date: Friday 9<sup>th</sup> June

Time

00:00


10:30 Alongside Fairlie

13:00 Clear of vessel

Total km of completed lines: 2183

	Today (hours)	Total (hours)
Mob/demob, setting up	2.50	40.75
On line	0.00	258.50
Turning	0.00	37.25
Steaming	10.50	148.25
Weather downtime	0.00	14.50
Equipment downtime	0.00	0.00
Vessel downtime	0.00	0.00
Port	0.00	33.25

## Appendix 3 Line Summary Log Sheet

British Geological Survey Marine Operations								Line Summary Log Sheet 1 of 1								Vessel: RRS Charles Darwin CD180	
PROJECT		BGS06/02		Area: Rockall-Hatton-Faroes				Type: Geophysical Survey				 <b>British Geological Survey</b> <small>NATURAL ENVIRONMENT RESEARCH COUNCIL</small>					
Line		Start		End		Length	Total	Equipment run							Comments		
No.	Dir	Date	Time	Date	Time	(km)	(km)	Airgun	Sparker	Maggy	Gravity	Pinger	PES	Multi-beam			
1	NW	24.05.06	06:32	25.05.06	06:53	308.00	308.00				X	X	X	X	Seastate poor at SOL, good at EOL		
2	SE	25.05.06	10:09	25.05.06	12:33	15.00	323.00	X	X	X	X	X	X	X	Seastate good, ocean swell		
3	NW	25.05.06	13:02	25.05.06	15:10	15.00	338.00	X	X	X	X	X	X	X	Seastate good, ocean swell		
4	SW	25.05.06	17:08	25.05.06	19:00	15.00	353.00	X	X	X	X	X	X	X	Seastate moderate to good, ocean swell		
5	NE	25.05.06	20:26	25.05.06	22:28	14.00	367.00	X	X	X	X	X	X	X	Seastate moderate to good, ocean swell		
6	N	26.05.06	01:44	26.05.06	06:10	33.50	400.50	X	X	X	X	X	X	X	Seastate moderate to good, ocean swell		
7	N	26.05.06	06:12	26.05.06	08:35	19.00	419.50	X	X	X	X	X	X	X	Seastate moderate to good, ocean swell		
8	N	26.05.06	08:38	26.05.06	11:14	19.00	438.50	X	X	X	X	X	X	X	Seastate moderate to good, ocean swell		
9	SE	26.05.06	12:00	26.05.06	15:28	26.00	464.50	X	X	X	X	X	X	X	Seastate moderate to good, ocean swell		
10	N	26.05.06	15:53	26.05.06	20:26	35.00	499.50	X	X	X	X	X	X	X	Seastate good, ocean swell		
11	E	26.05.06	21:18	27.05.06	06:32	70.00	569.50	X	X	X	X	X	X	X	Seastate good, ocean swell		
12	NE	27.05.06	18:47	29.05.06	20:03	375.00	944.50	X	X	X	X	X	X	X	Seastate variable, moderate to poor		
13	SW	30.05.06	01:54	30.05.06	16:23	66.00	1010.50	X	X	X	X	X	X	X	Seastate variable, moderate, improving		
14	NE	30.05.06	17:03	31.05.06	03:25	60.00	1070.50	X	X	X	X	X	X	X	Seastate good, ocean swell		
15	SW	31.05.06	04:46	01.06.06	10:17	230.00	1300.50	X	X	X	X	X	X	X	Seastate good, ocean swell		
16	N	01.06.06	11:22	02.06.06	18:58	245.00	1545.50	X	X	X	X	X	X	X	Seastate poor, ocean swell deteriorating		
17	E	02.06.06	19:44	03.06.06	06:03	87.00	1632.50	X	X	X	X	X	X	X	Seastate poor, ocean swell improving		
18	SE	03.06.06	06:16	03.06.06	15:53	80.00	1712.50	X	X	X	X	X	X	X	Seastate reasonable, ocean swell, improving		
19	N	03.06.06	16:21	04.06.06	01:46	70.00	1782.50	X	X	X	X	X	X	X	Seastate good, ocean swell		
20	SW	04.06.06	02:28	04.06.06	20:22	131.00	1913.50	X	X	X	X	X	X	X	Seastate good, ocean swell		
21	SW	04.06.06	20:22	05.06.06	16:18	160.00	2073.50	X	X	X	X	X	X	X	Seastate good, little ocean swell		
22	NE	06.06.06	18:40	06.06.06	19:24	5.10	2078.60		X		X	X	X	X	Seastate good, little ocean swell		
23	S	06.06.06	19:50	06.06.06	20:11	2.70	2081.30		X		X	X	X	X	Seastate good, little ocean swell		
24	N	06.06.06	20:18	06.06.06	20:41	2.70	2084.00		X		X	X	X	X	Seastate good, little ocean swell		
25	S	06.06.06	20:50	06.06.06	21:14	2.70	2086.70		X		X	X	X	X	Seastate good, little ocean swell		
26	E	06.06.06	21:44	06.06.06	22:04	2.50	2089.20		X		X	X	X	X	Seastate good, little ocean swell		
27	SE	07.06.06	07:54	07.06.06	10:18	15.30	2104.50		X		X	X	X	X	Seastate good, little ocean swell		
28	SW	07.06.06	10:50	07.06.06	12:57	14.50	2119.00		X		X	X	X	X	Seastate good, little ocean swell		
29	NE	07.06.06	13:22	07.06.06	15:10	14.50	2133.50		X		X	X	X	X	Seastate good, little ocean swell		
30	SE	07.06.06	15:39	07.06.06	22:04	50	2183.50		X		X	X	X	X	Seastate good, little ocean swell		

## Appendix 4 Gravity Base Ties

<b>Date</b>	<b>Location</b>	<b>Corrected Ship Base (mgals)</b>	<b>Still Meter Reading</b>	<b>Corrected Meter Value (0.9911 x meter Reading, mgals)</b>
18 <sup>th</sup> May 2006	Falmouth	981089.8	11811.2	11706.1
9 <sup>th</sup> June 2006	Fairlie	981581.0	12305.5	12196.0

	<b>Falmouth (mgals)</b>	<b>Fairlie (mgals)</b>	<b>Difference between locations (mgals)</b>
<b>Corrected Ship Base</b>	981089.8	981581.0	-491.2
<b>Corrected Meter Value</b>	11706.1	12196.0	-489.1
<b>Calculated Drift</b>	-	-	+2.1

### Notes:


The vessel had two complete blackouts during the cruise and hence loss of electrical power to the gravity meter system. Observations at the time indicated that this did not affect the gravity readings and hence no 'tear' at this point.






## Appendix 5 Time Utilisation Diagrams

### TIME UTILISATION IN THE SURVEY AREA

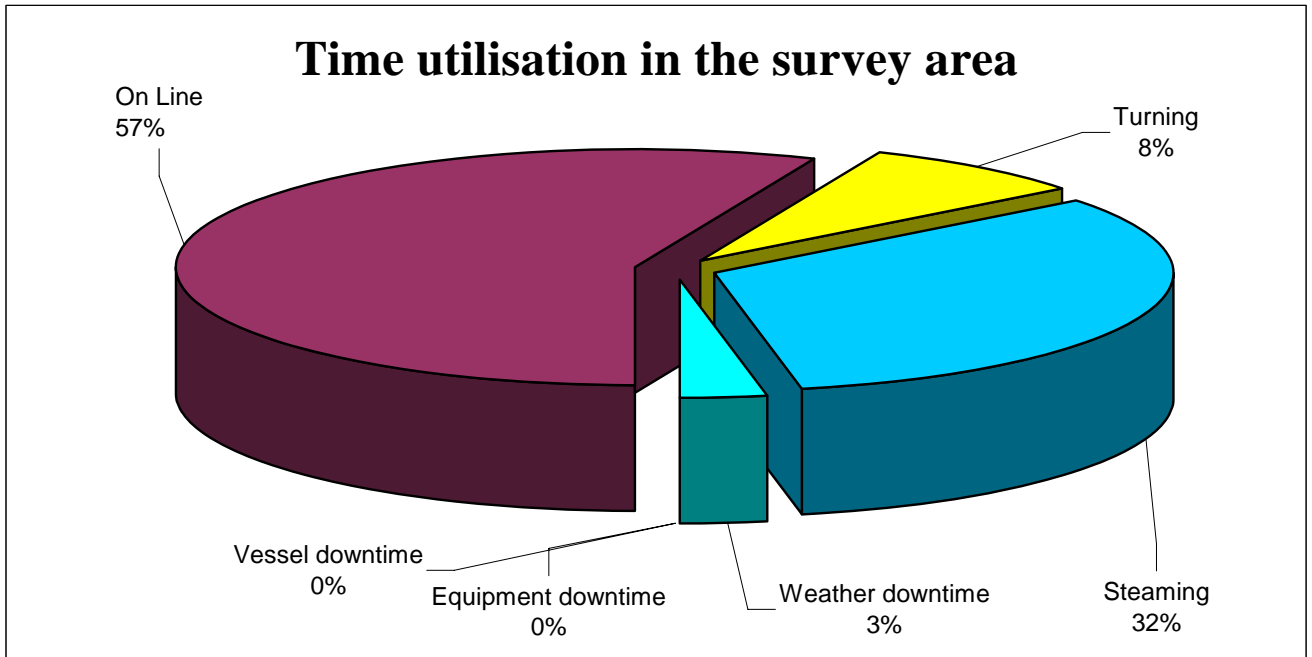

### TIME UTILISATION FOR TOTAL SHIP TIME

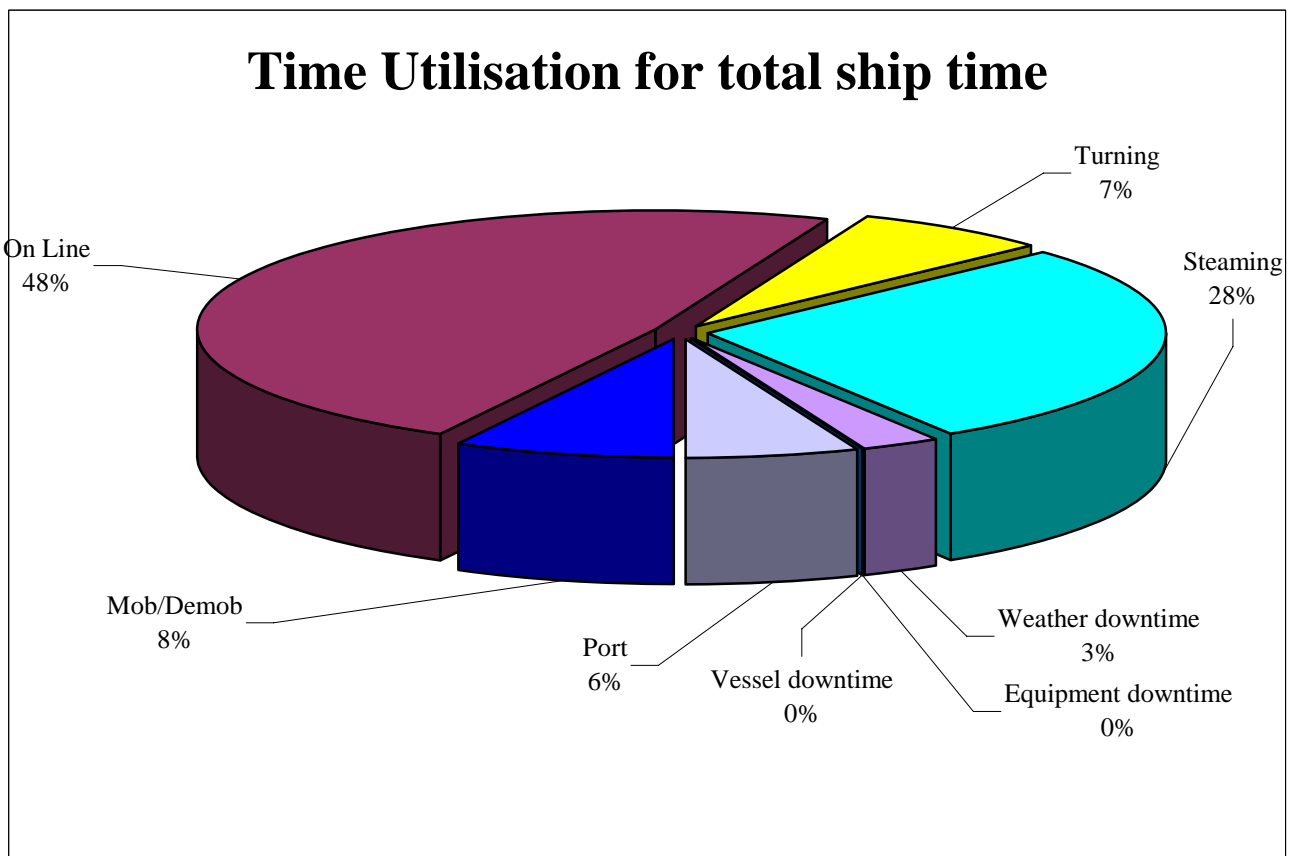

## Abbreviations

<i>BCD</i>	Binary Coded Decimal
<i>BGS</i>	British Geological Survey
<i>EOL</i>	End of line
<i>ETS</i>	Electronic and Technical Support
<i>GMT</i>	Greenwich Mean Time
<i>IT</i>	Information Technology
<i>NOC</i>	National Oceanographic Centre
<i>PES</i>	Precision Echosounder
<i>RSU</i>	Research Ship Unit
<i>SVP</i>	Sound Velocity Probe
<i>SOL</i>	Start of line
<i>TVF</i>	Time Varied Filter
<i>TVG</i>	Time Varied Gain
<i>UKORS</i>	United Kingdom Ocean Research Services
